ID	Task Name	Duration	Start	Finish
1	SHORT TERM EXPOSURE STUDY	337 days	Thu 11/1/01	Fri 2/14/03
2	investigator's brochure	15 days	Thu 11/1/01	Wed 11/21/01
3	study objectives	5 days	Thu 11/1/01	Wed 11/7/01
4	draft protocol summary/study plan	10 days	Thu 11/8/01	Wed 11/21/01
5	site selection	15 days	Thu 11/22/01	Wed 12/12/01
6	1st contract with site	30 days	Thu 12/13/01	Wed 1/23/02
7	protocol development, informed consent	50 days	Thu 1/24/02	Wed 4/3/02
8	final protocol	0 days	Wed 4/3/02	Wed 4/3/02
9	IRB review	50 days	Thu 4/4/02	Wed 6/12/02
10	bioanalytical methods set up	120 days	Thu 11/1/01	Wed 4/17/02
11	2nd contract with site	20 days	Thu 4/4/02	Wed 5/1/02
12	recruitment and screening	42 days	Thu 6/13/02	Fri 8/9/02
13	IRB approval	0 days	Wed 6/12/02	Wed 6/12/02
14	test materials available	0 days	Mon 7/1/02	Mon 7/1/02
15	clinical performance	15 days	Mon 8/12/02	Fri 8/30/02
16	lab analysis	70 days	Mon 9/2/02	Fri 12/6/02
17	data management	10 days	Mon 12/9/02	Fri 12/20/02
18	draft report	20 days	Mon 12/23/02	Fri 1/17/03
19	results available	0 days	Fri 1/17/03	Fri 1/17/03
20	final report	20 days	Mon 1/20/03	Fri 2/14/03
21	final results	0 days	Fri 2/14/03	Fri 2/14/03

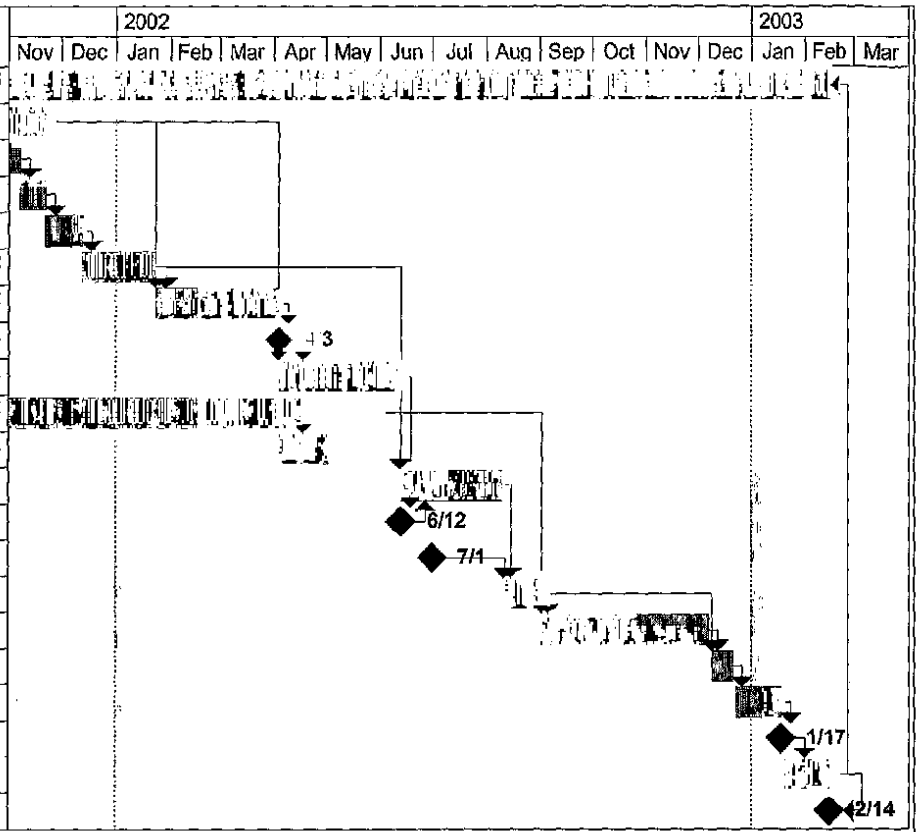

Project: ClinDevSCoR02
Date: Wed 10/17/01

Task	Rolled Up Task	External Tasks	
Progress	Rolled Up Milestone	Project Summary	
Milestone	Rolled Up Progress	External Milestone	
Summary	Split	Deadline	

PM30013373346

Source: https://www.industrydocuments.ucsf.edu/docs/gxvk0001
